




## CONSTRUCTION REPORT December 2018

---

### Osceola Campus

#### **Center for Accelerated Training (CAT)**

- Substantial Completion 11/02/2018
- Furniture and Technology installation
- Occupancy second week of December

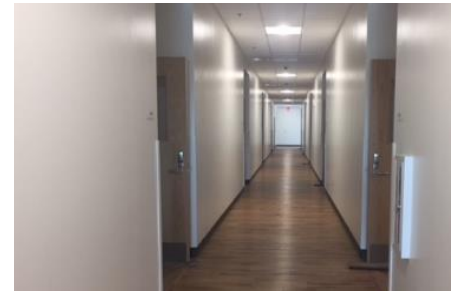

#### **Career in Technology**

- Building foundation underway.
- Substantial Completion December of 2019
- Occupancy January 2020



### Downtown Campus

#### **Union West (Student Services, Culinary & Hospitality Building)**

- Structure including parking complete
- Exterior skin and glazing proceeding on schedule
- Interior utilities rough-ins and wall framing are in progress
- Substantial completion May 2019
- Occupancy August 2019



#### **UCF Academic Commons**

- Schedule concerns, implementing recovery plan
- Exterior precast panels being installed
- Interior utilities rough-ins and wall framing are in progress
- Garage construction start and completion delayed
- Building Occupancy August 2019, Garage Occupancy TBD

