



CONSTRUCTION REPORT June 2018

East Campus: Building 1B Interior Renovation

- Drywall finishing and MEP rough-ins are completed
- Installing ceiling and priming walls
- Substantial completion July 25, 2018
- Occupancy August 2018



Osceola Campus: Center for Accelerated Training (CAT)

- Foundations and underground utilities are in progress, started masonry
- Substantial completion November 2018
- Occupancy January 2019



Osceola Campus: Career in Technology Building (CIT)


- Construction documents complete – Project out to bid
- Guaranteed Maximum Price (GMP) proposal June 2018
- Substantial completion December of 2019
- Occupancy January 2020



Downtown Campus

Union West (Student Services, Culinary & Hospitality Building):

- Pouring of elevated slabs has progressed to the seventh floor
- Construction on schedule
- Substantial completion May 31, 2019
- Occupancy August, 2019

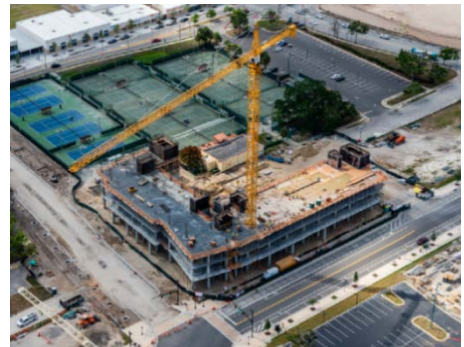

UCF Academic Commons:

- Second floor framing continues
- Implementing schedule recovery plan
- Occupancy August 2019
